

LAB 2: Agile Backlog Creation & Sprint Simulation in Jira

Student Name: DIYA AGARWAL
SRN: PES1UG24AM096

Project: Smart Hostel Management System

EPIC 3: Ticket Status Updates & Notifications

 HMT-3



 1







Ticket Status Updates & Notifications

To Do ▾





 Improve Epic



Description: Enable staff and wardens to update ticket progress and automatically notify the resident of status changes.

Child work items

100% Done

Work	Prio...	Ass...	Status
 HMT-17 Update Ticket Status	 M.	 Ur	Done ▾
 HMT-18 Add Work Notes / Photos	 M.	 Ur	Done ▾
 HMT-19 Notify Resident of Status Change	 M.	 Ur	Done ▾

Total story points = 5+3+3 = 11 points

2. User Stories (Detailed)

a) Update Ticket Status - As a Maintenance Staff member or Warden, I want to update the status of a ticket (e.g., Open, In Progress, Resolved), so that the progress of the work is always visible.

Assignee	 Unassigned Assign to me
Parent	  HMT-3 Ticket Status Updates & Notification
Sprint	Add sprint 
Labels	Add labels
Due date	Add due date
Team	Add team
Start date	Add date
Story point estimate	

b) Add Work Notes / Photos - As a Maintenance Staff member, I want to add work notes and photos to a ticket, so that there is a clear record of the work done and proof of the fix.

Assignee	 Unassigned Assign to me
Parent	  HMT-3 Ticket Status Updates & Notification
Sprint	Add sprint 
Labels	Add labels
Due date	Add due date
Team	Add team
Start date	Add date
Story point estimate	

c) Notify Resident of Status Change - As a Resident, I want to be notified automatically whenever the status of my ticket changes, so that I stay informed without having to check manually.


Assignee	 Unassigned Assign to me
Parent	  HMT-3 Ticket Status Updates & Notification
Sprint	Add sprint 
Labels	Add labels
Due date	Add due date
Team	Add team
Start date	Add date
Story point estimate	

BURNDOWN CHART –

Sprint 1



Sprint 2

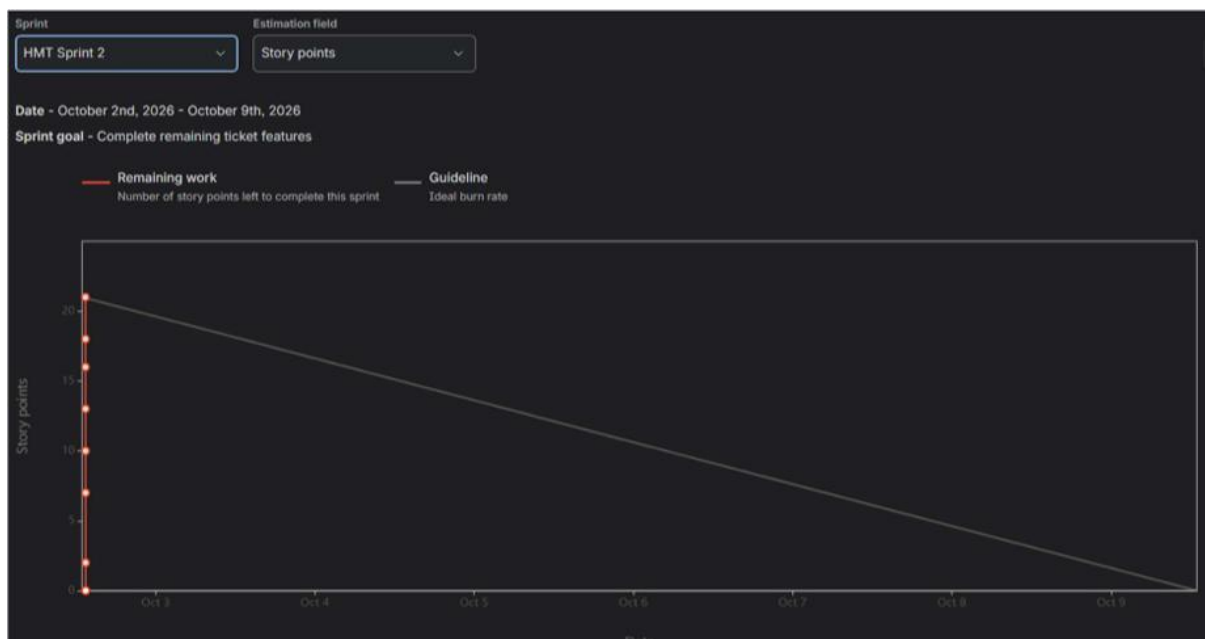

3. Reflect on Answers

1. Did your estimations reflect the actual effort?

Yes, the estimations largely reflected the actual effort. The story points were assigned using the Fibonacci scale during a Planning Poker session with the team. "Update Ticket Status" (HMT-17) received 5 points because it involves the status workflow and transition logic, role-based permission checks for staff and wardens, and updating the ticket record. "Add Work Notes / Photos" (HMT-18) and "Notify Resident of Status Change" (HMT-19) each received 3 points as they were moderately complex but fairly independent features. The photo attachment part of HMT-18 carried the most uncertainty because of file size handling and storage considerations, so it could be re-estimated higher in future. However, overall the estimations were within an acceptable range.

2. Was your backlog well-prioritized?

The backlog was well-prioritized for the ticket tracking workflow. All three user stories were marked as Medium priority because they collectively form the core of the status update and notification feature. HMT-17 (Update Ticket Status) was placed at the top as it is the foundational story - without a status change, there is nothing to document or notify about. HMT-18 (Add Work Notes / Photos) followed as it adds context and evidence to each status update. HMT-19 (Notify Resident of Status Change) came last because it depends on status changes being recorded successfully. In future sprints, we would prioritize more granularly based on user feedback and business value.

3. How did your simulated sprint align with your plan?

The simulated sprint aligned well with the plan. All three user stories were moved from To Do to In Progress to Done, and the epic shows 100% of its child work items as Done. The team was able to complete all 11 story points, meeting the goal of letting staff and wardens update ticket progress and notifying residents automatically. There were no major blockers, though the work notes and photo upload story needed the most attention. The sprint board showed a clean progression from start to finish.

4. What insights did the burndown chart give about your team's capacity?

The burndown charts show the work committed in each sprint (26 story points in Sprint 1 and 21 in Sprint 2) against the ideal guideline, which helps in judging how much the team can take on at a time. The 11 points of this epic fit comfortably within that capacity, and all committed work was completed by the end of the sprint, which is a positive sign for sprint planning accuracy. The insight for future sprints is that technically uncertain tasks, such as photo upload and notifications, should either be given more time or be broken into smaller subtasks. Based on this baseline, the team can consider committing to a similar or slightly higher load in the next sprint.
